



**ASTM D6938 In-Place Density and Water Content of Soil and
Soil-Aggregate by Nuclear Methods (Shallow Depth)**

Project: Veterans Salcha Cemetary
Salcha, AK
Client: H.C. Contractor

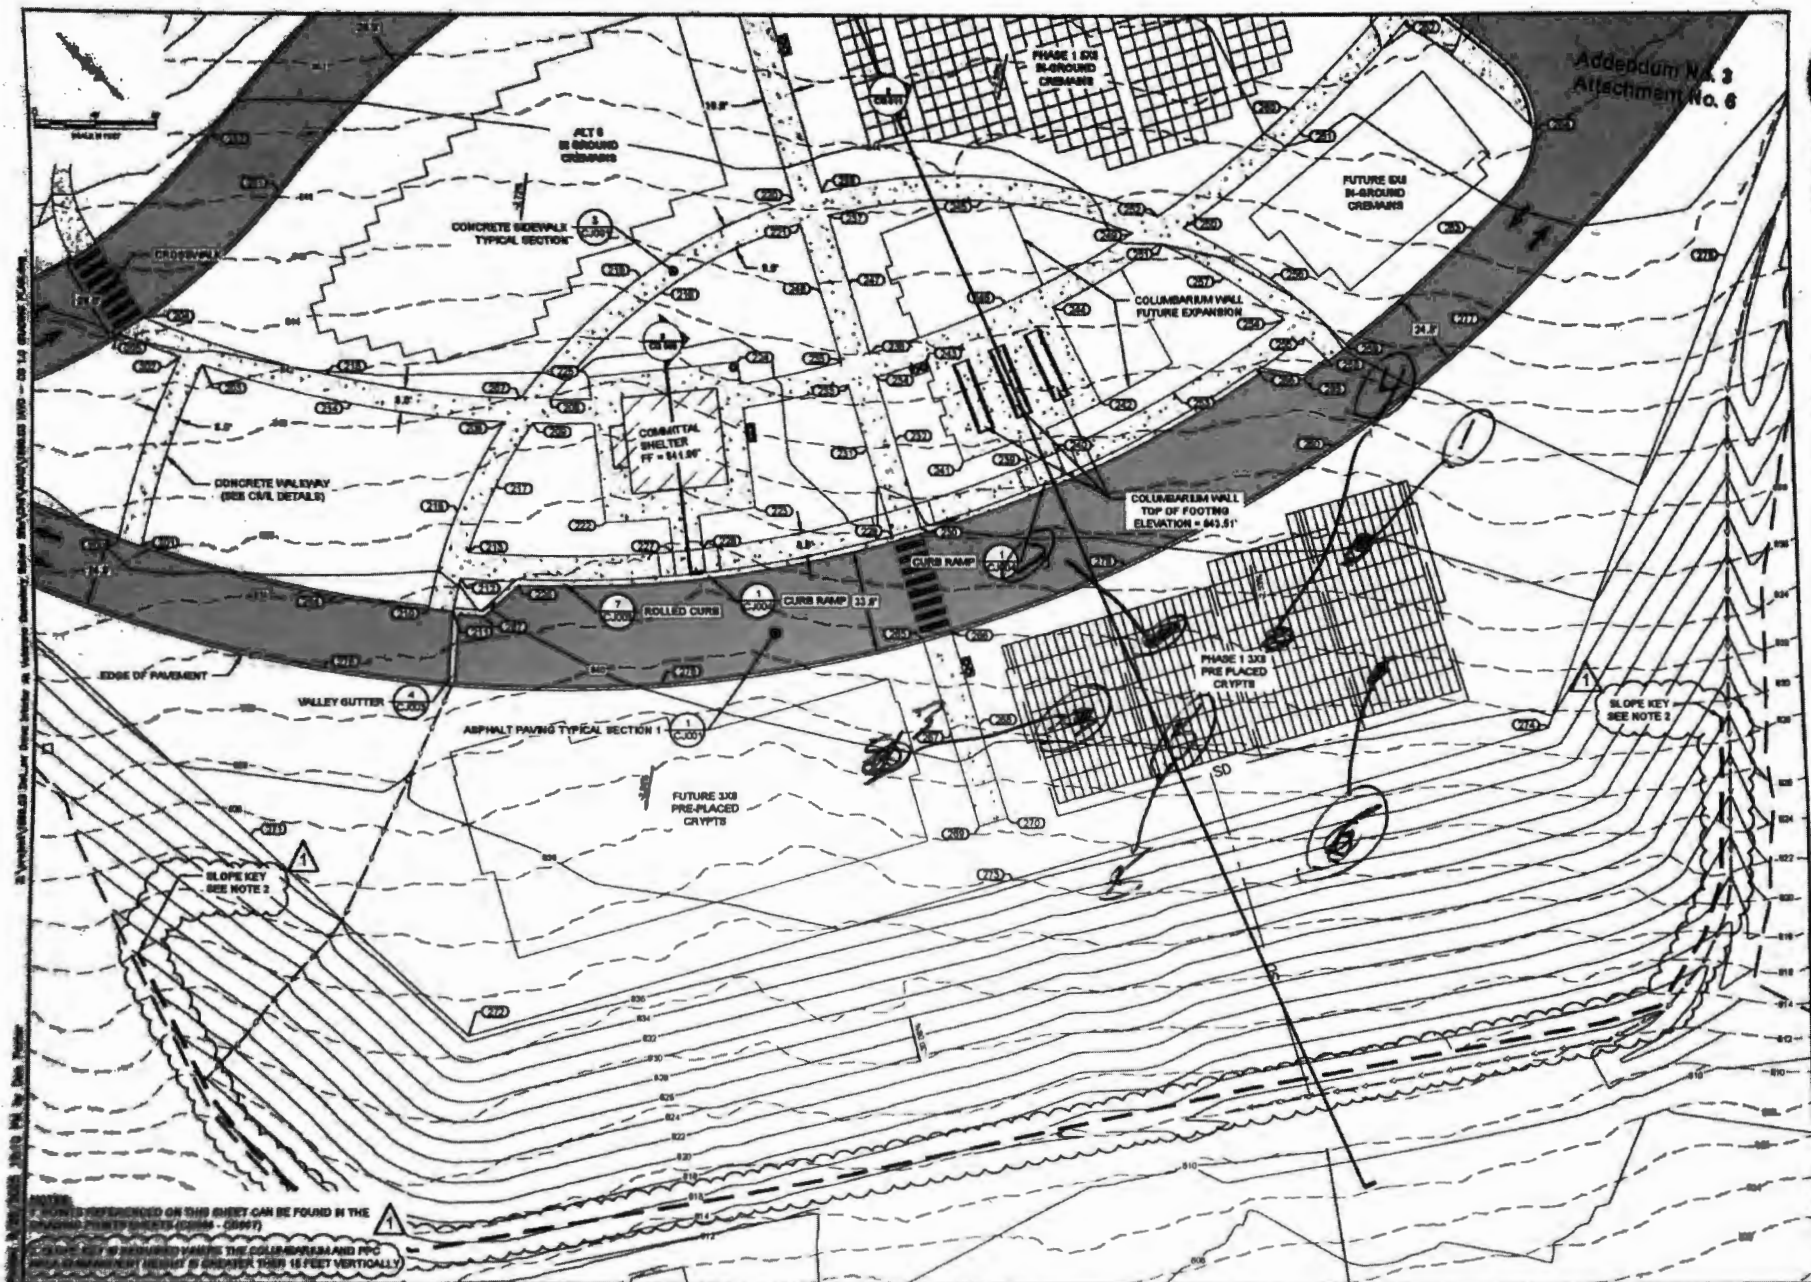
Project #: 2026-012
Date: June 23, 2026
Area Tested: Cypts

Material / Source:
3" minus/ Rolling stone 146.6

Gauge: Instrotek 3500
Operator: Paul Gerber

Ser: # 1095

Test #	Soil Type	Test Depth(in)	Lift Elev	Location	Wet Density	% Moist.	Dry Density	Max Density	Percent Density	Required Density
1	3" minus	8"	top classified	Cypts (see map)	152.4	6.3	143.4	146.6	97.8%	95%
2	3" minus	8"	top classified	Cypts (see map)	150.7	5.9	142.3	146.6	97.1%	95%
3	3" minus	8"	top classified	Cypts (see map)	146.6	4.6	140.2	146.6	95.6%	95%
4	3" minus	8"	top classified	Cypts (see map)	143.7	6.0	135.6	146.6	92.5%	95%
5	3" minus	8"	top classified	Cypts (see map)	149.4	5.7	141.3	146.6	96.4%	95%
6	3" minus	8'	top classified	Cypts (see map)	151.2	6.2	142.4	146.6	97.1%	95%

[illegible]

FOR INFORMATION PURPOSES ONLY
THIS IS CONFIDENTIAL AND
NOT BE DISCLOSED TO ANY
PERSON OR ENTITY
OTHER THAN THE
PERSON TO WHOM IT IS
ADDRESSED

TRANSPORTATION AND
PUBLIC FACILITIES

DEPARTMENT OF
PUBLIC
DEPARTMENT

[illegible]

VETERANS
CENTRAL

RIOR ALASKA V
TERY (IAVC)
OF PROJECT NO: RSAQ
ING PI AN 2 - 0

INTER	FILE	
CEME	CLASS OF	
AKDOTAS	PERIOD	
CRAD	DATE	

15 of 16
